



UPDATE ON CONSTRUCTION PROGRESS AND FINANCES

East, West, and South High Schools as
well as Millcreek Elementary

October 8, 2026

CONSTRUCTION FINANCE UPDATE

Funding Sources									
General Fund Balance Reserved for Construction				\$14,000,000					
Fund 30 Capital Balance				\$10,000,000					
2025 Bond Fund				\$45,000,000					
				\$69,000,000					
		</							

CONSTRUCTION SCHEDULES



Construction

- Minor Punchlist Items in Completion



Construction

- Moving into Ceramic and Art classrooms this week
- Working on Punchlist Item Completion



Construction

- Addition Completion 6/14/27
- Summer Interior Work 6/14/27-8/14/27
- Project Substantial Completion 8/14/27




Construction

- Project Complete

CB WEST

MACFARLANE LANE

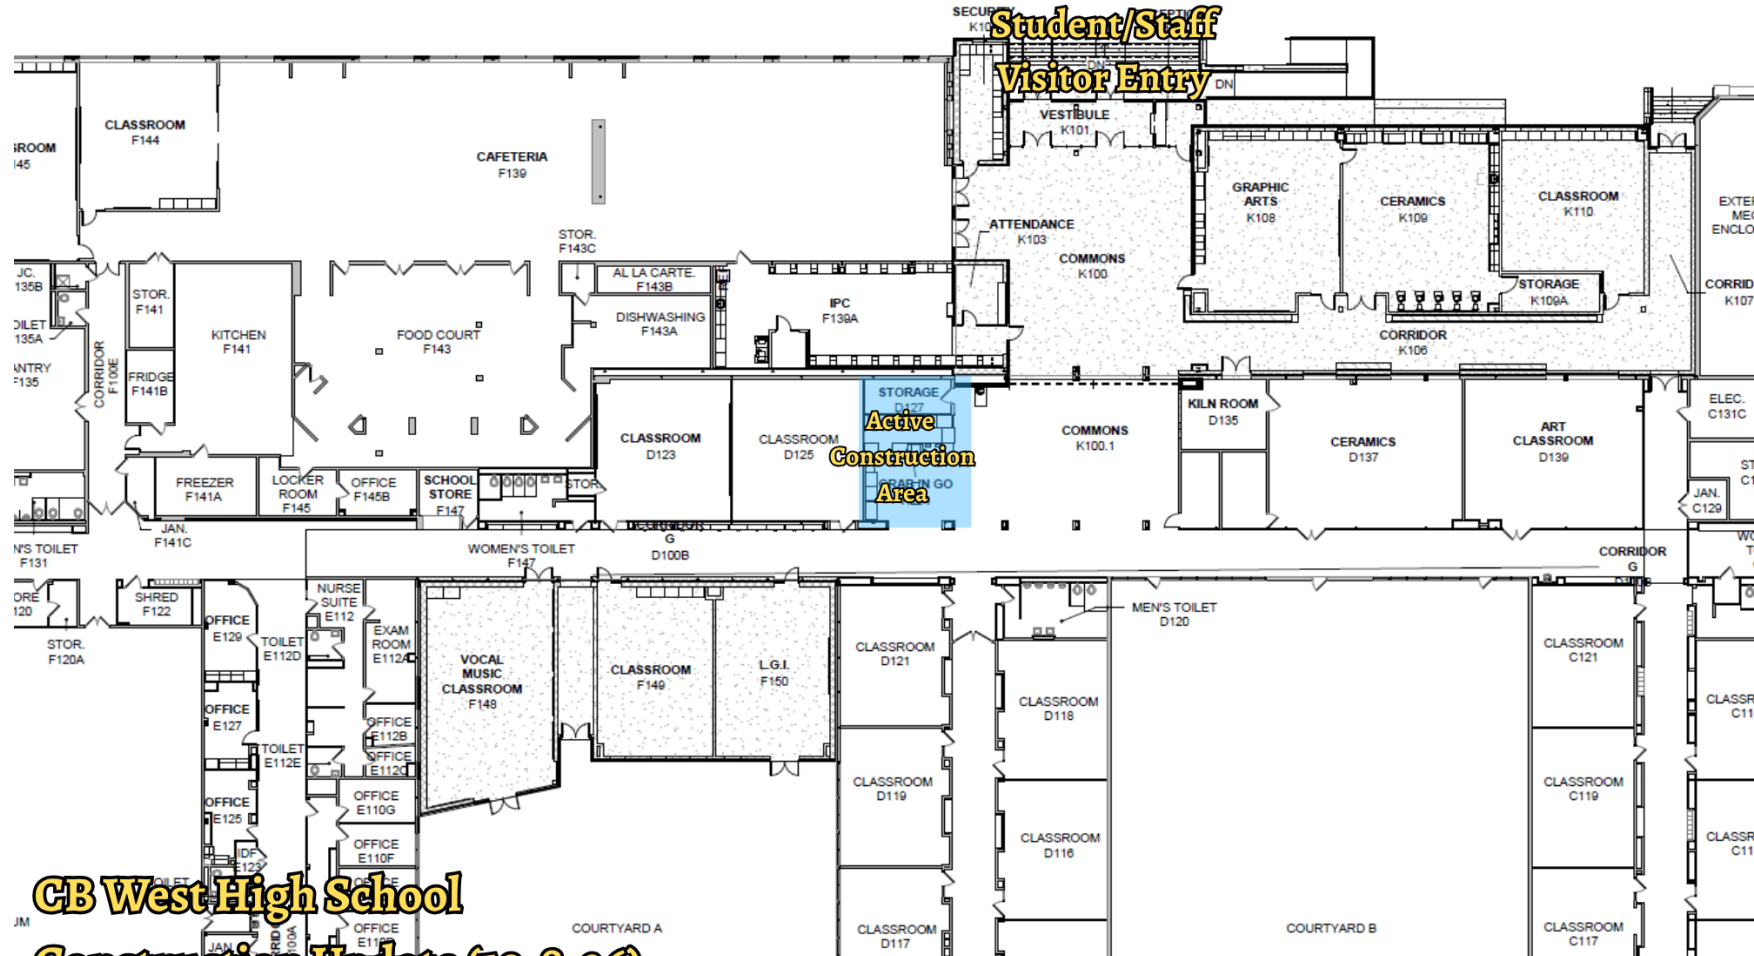

CB West High School
Construction Update (10-8-26)

PICTURES FROM WEST CONSTRUCTION

